

MARCH 28, 2023

Illinois Tollway 2023 Overview

Mohamad Faraj, Executive Project Manager

MOVE ILLINOIS STATUS | 2012 - 2022

12th year of 15-year, \$14 billion capital program



**70.5%
COMPLETE**

**\$12 BILLION
COMMITTED**

**117,740
JOBS**

**786 CONTRACTS
AWARDED**

**521 CONTRACTS
CLOSED OUT**

NOTABLE PROJECTS DELIVERED IN 2022

Tri-State Tollway (I-294)/I-57 Interchange




32,000 tons of asphalt



16,000 tons of steel



753,000 tons of earthwork moved

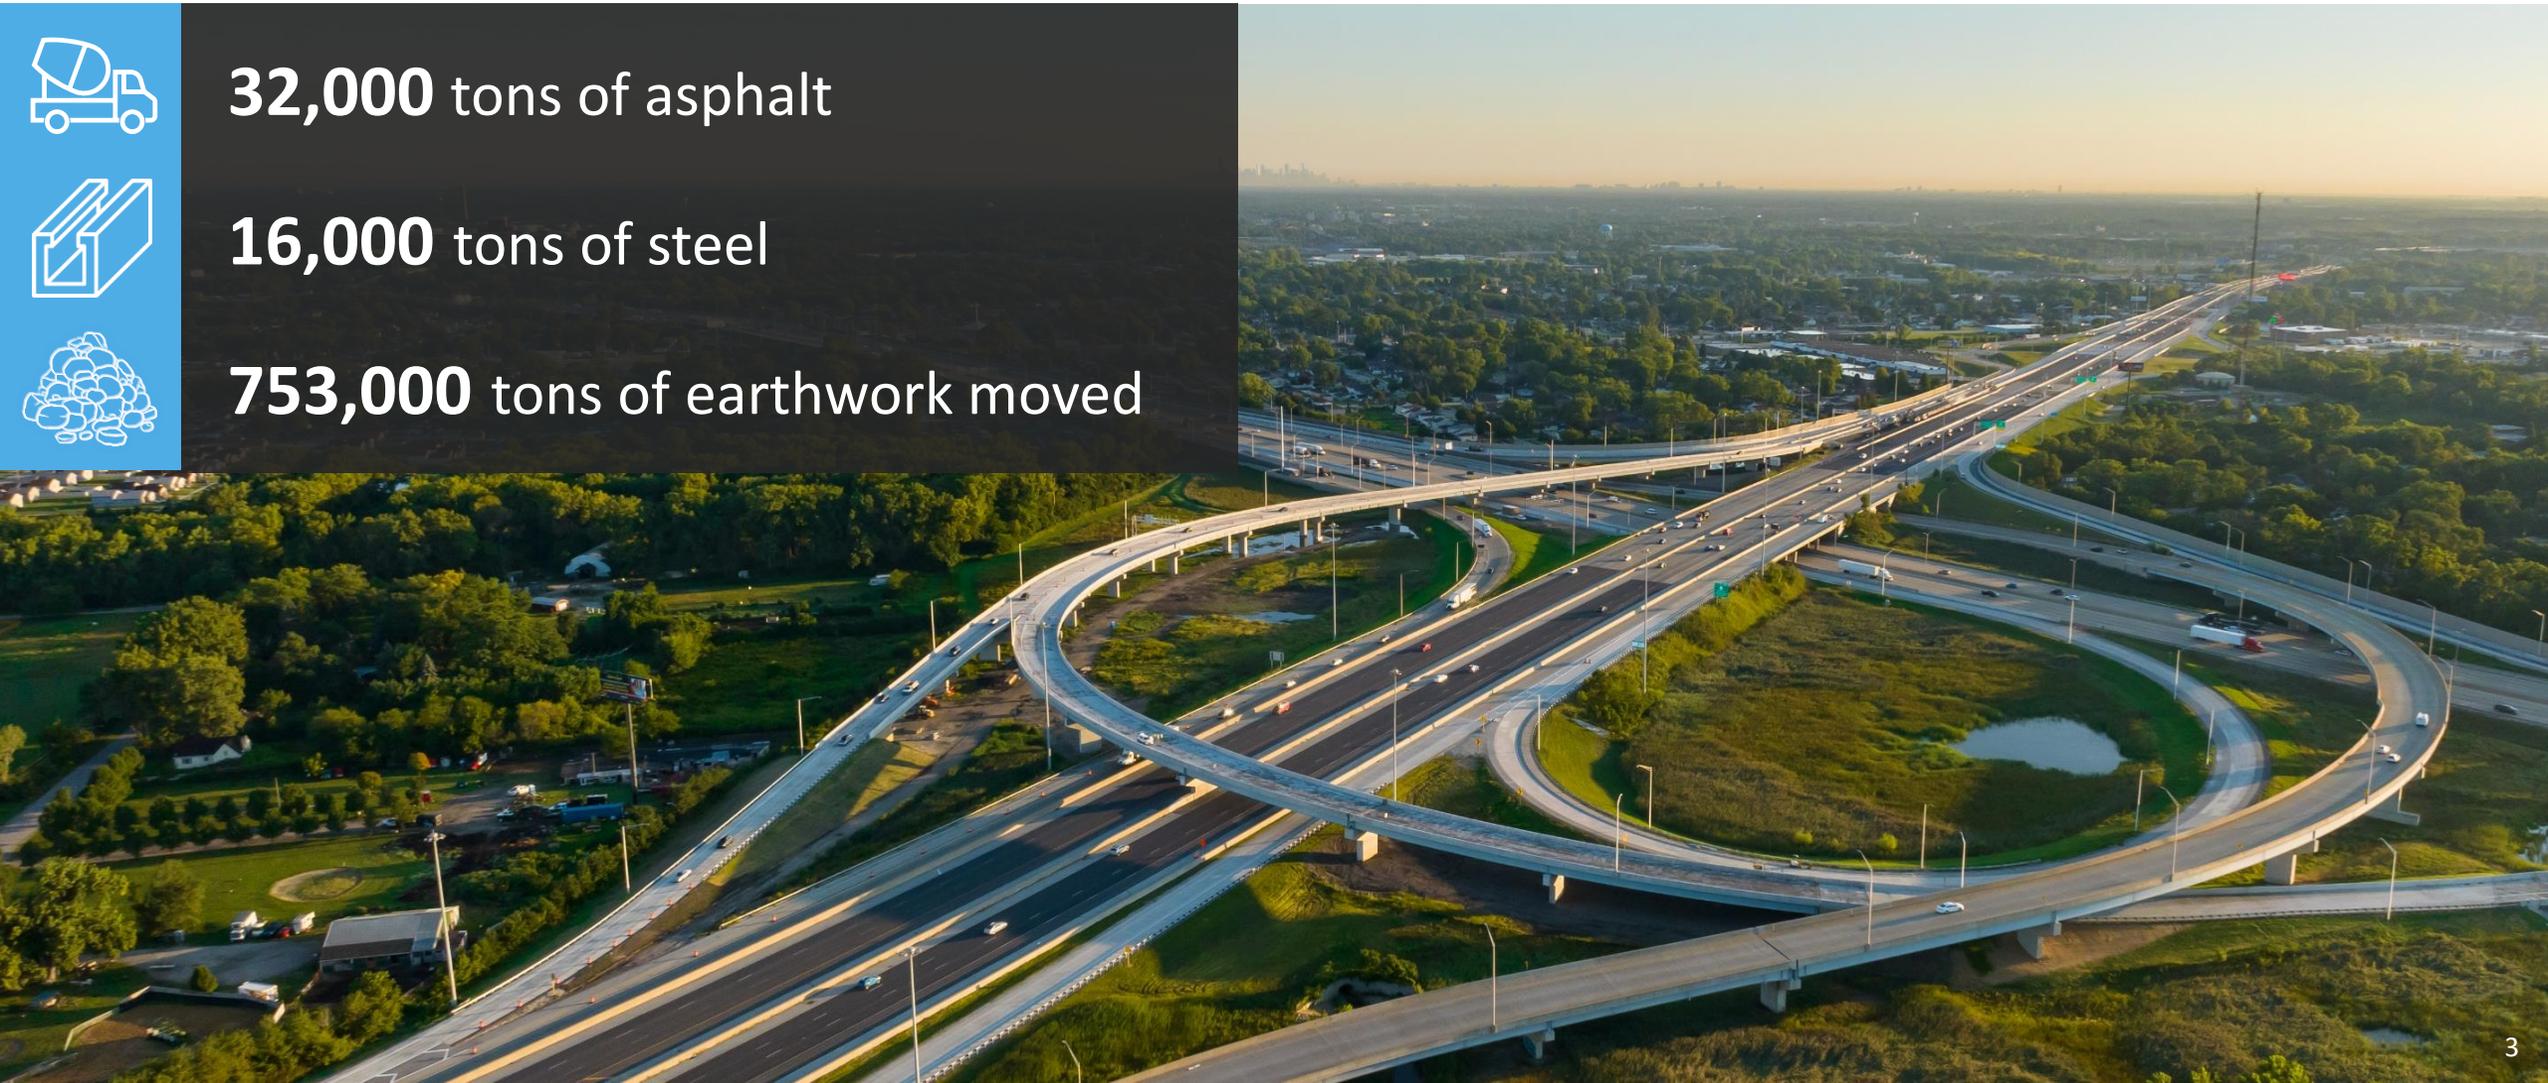

NOTABLE PROJECTS DELIVERED IN 2022

I-294 Mile Long Bridge



28,000 tons of asphalt



19 million pounds of reinforcing steel



189,000 tons of earthwork moved



2023 CAPITAL PROGRAM HIGHLIGHTS

Approximately **\$1.47 billion** allocated for the Move Illinois Program in 2023



Tri-State Tollway (I-294)

\$615.3 million

Roadway widening and reconstruction

I-290/I-88 Interchange at I-294 reconstruction

Complete construction of the new southbound Mile Long Bridge and removal of the old structure



I-490 Tollway

\$506.3 million

Interchange construction

- I-490/I-90
- I-490/IL 390
- I-490/I-294

I-490 bridge construction

Continued design services



Systemwide

\$314.8 million

Bridge, pavement and safety improvements

Maintenance facility improvements

2023 KEY CONSTRUCTION ADVERTISEMENTS

Approximately **\$535 million** scheduled to advertise in 2023



CENTRAL TRI-STATE TOLLWAY (I-294)

- Southbound I-294/I-290/I-88 Interchange from Roosevelt Road to St. Charles Road
- Asphalt overlay and pavement markings between 95th Street and I-55
- Active traffic management system, ITS and fiber installation



I-490 TOLLWAY

- Franklin Avenue Interchange
- I-490 bridge construction – Touhy Avenue to I-90




SYSTEMWIDE IMPROVEMENTS

- Bridge repairs
- Pavement repairs
- DMS installation
- ITS improvements


UPCOMING ASPHALT WORK

95th Street to I-55

- Two composite pavement overlay contracts (northbound, southbound)
- 1.25 inch of IL-9.5 SMA Binder, 1.75 inches of IL-12.5 SMA-F Surface, Unmodified SMA shoulder surface
- 53,000 tons SMA
- 234,000 pounds of tack coat
- 170,000 lineal feet of longitudinal joint sealant

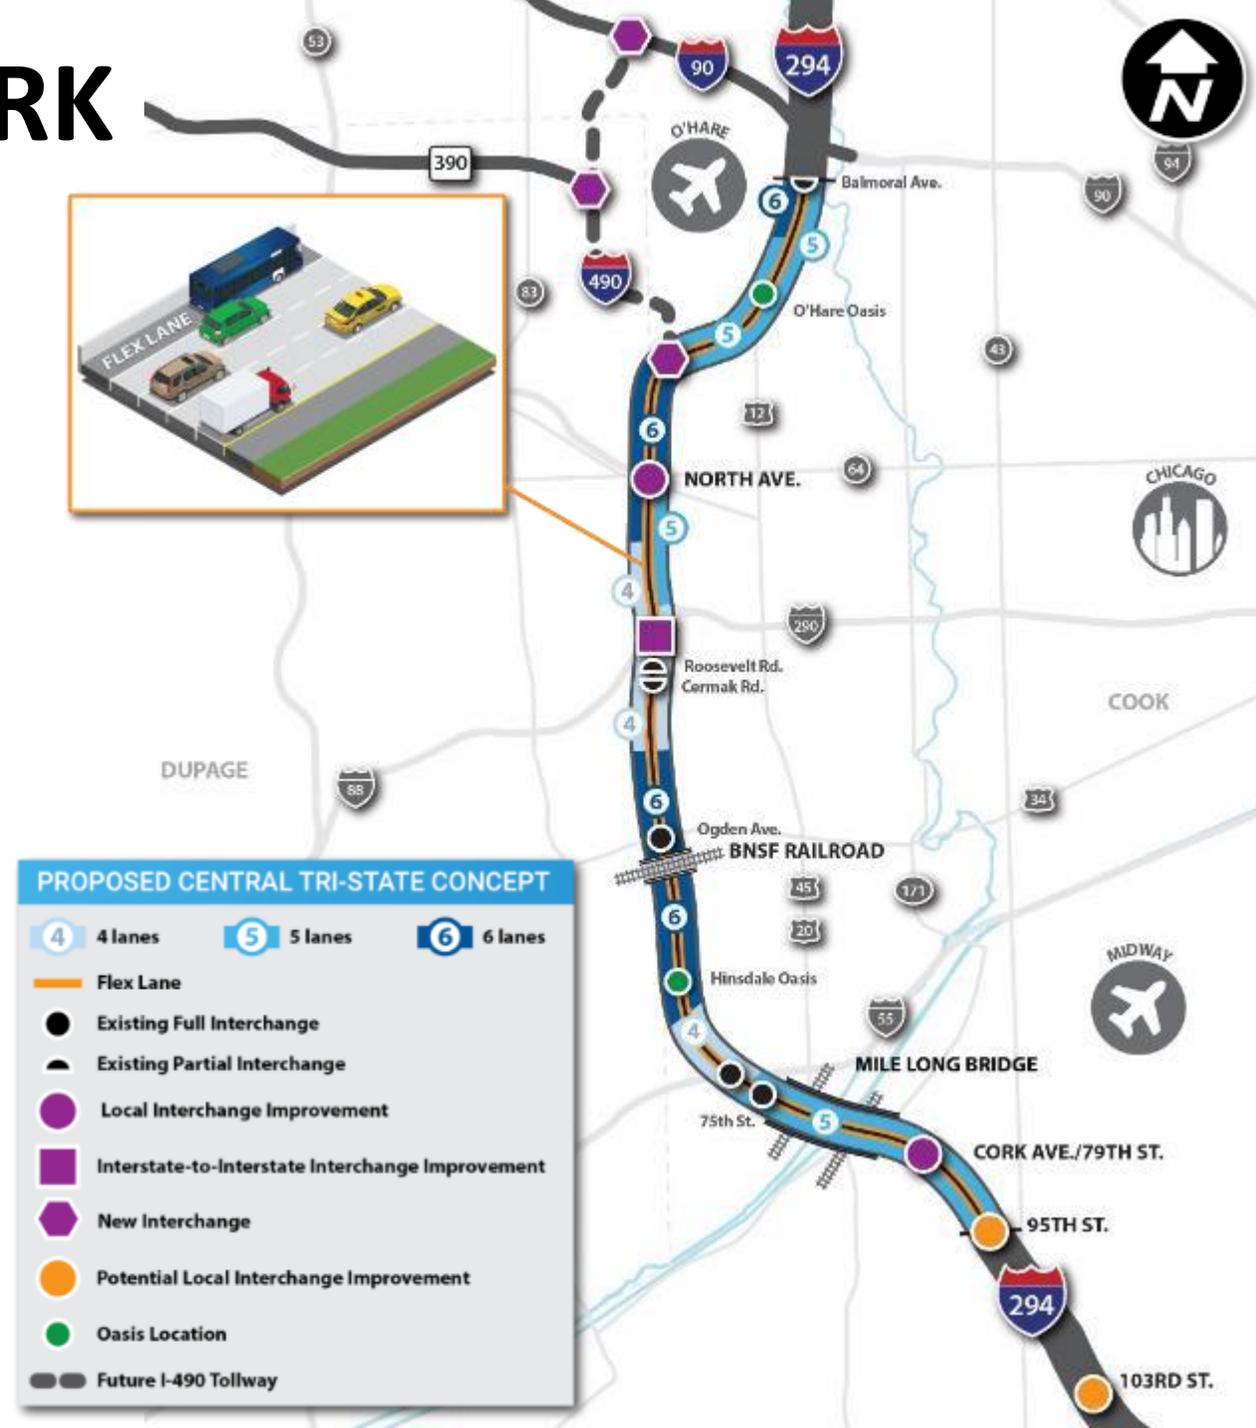

CTS CONTRACTOR QUANTITY REPORT

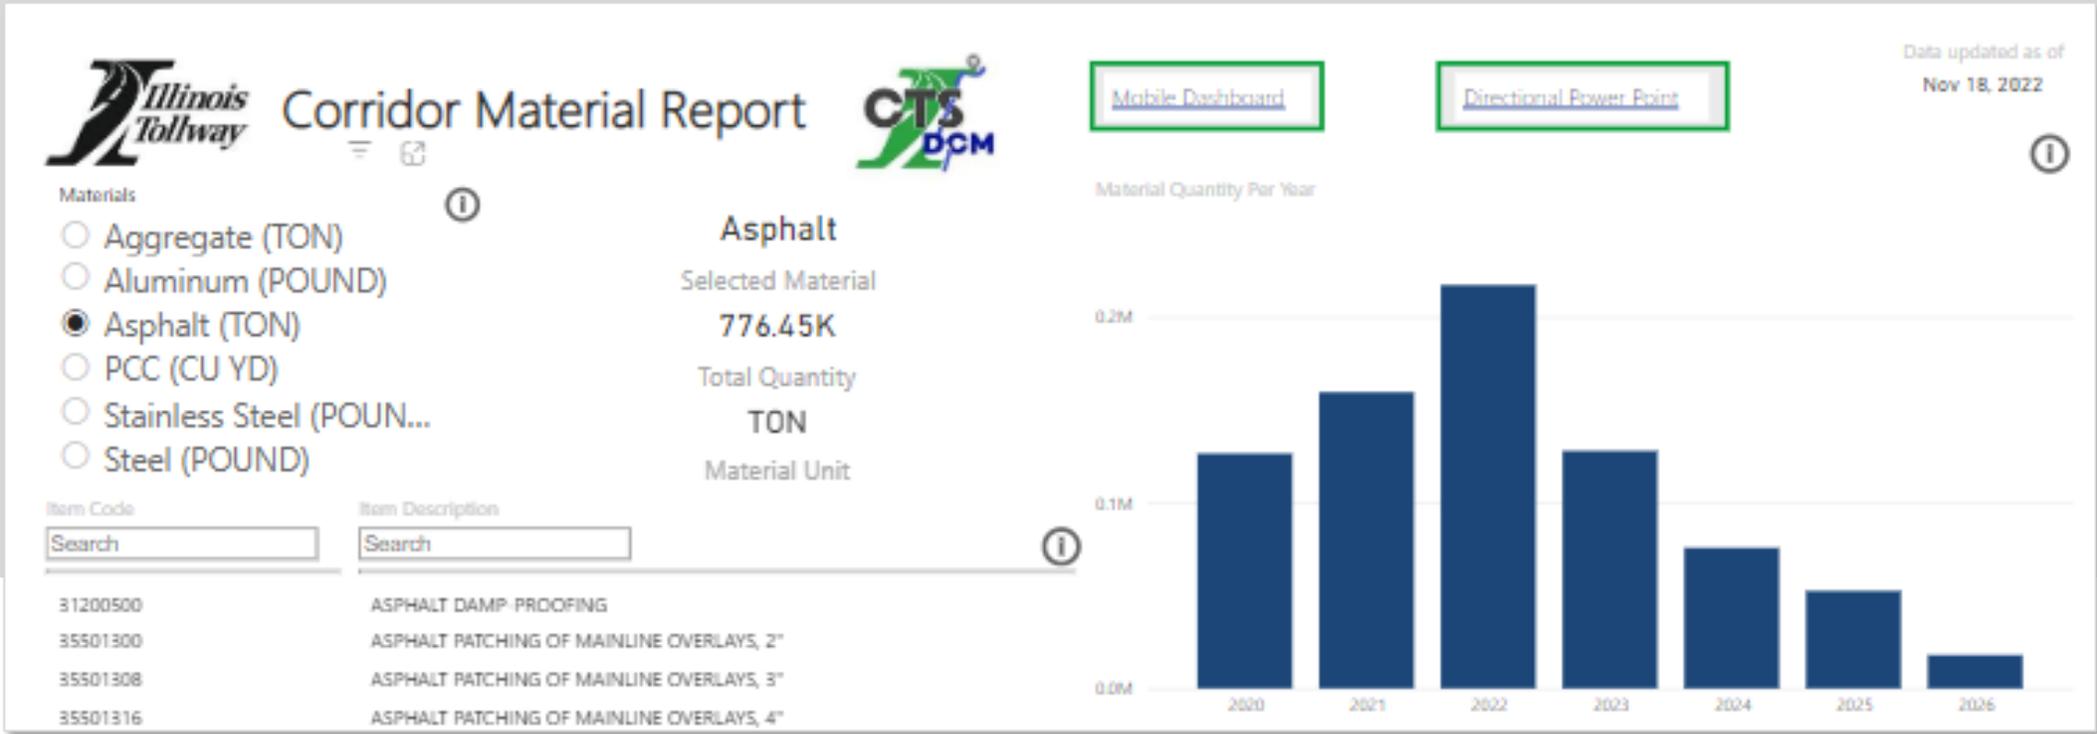

Visit **Doing Business > Construction and Engineering** at Illinoistollway.com to access the CTS Contractor Quantity Report

DOING BUSINESS

- Doing Business Overview
- Construction and Engineering**
- Construction and Engineering Overview
- Bids and Bulletins (PSBs)
- Contract Administration

Construction And Engineering Overview

This section serves as a central repository for Tollway engineering standards and publications.

Documents found on this site will principally be used by Tollway project managers to guide design section engineers and construction managers during design development and contract implementation. The most current and up-to-date documents adopted by the Tollway will be posted.

View construction pay estimates and professional services invoices for work completed on Illinois Tollway contracts.

i

- Construction Contract Tracker
- CTS Contractor Quantity Report**
- Earned Credit Program

E-TICKETING IMPLEMENTATION

Goal: Fully implemented by 2024

Encourage use on current and new 2023 contracts


- Allows for testing of systems
- Achieve comfort level for all users


Outreach to producers

- Asphalt
- Concrete
- Aggregate

Industry outreach

Specification changes

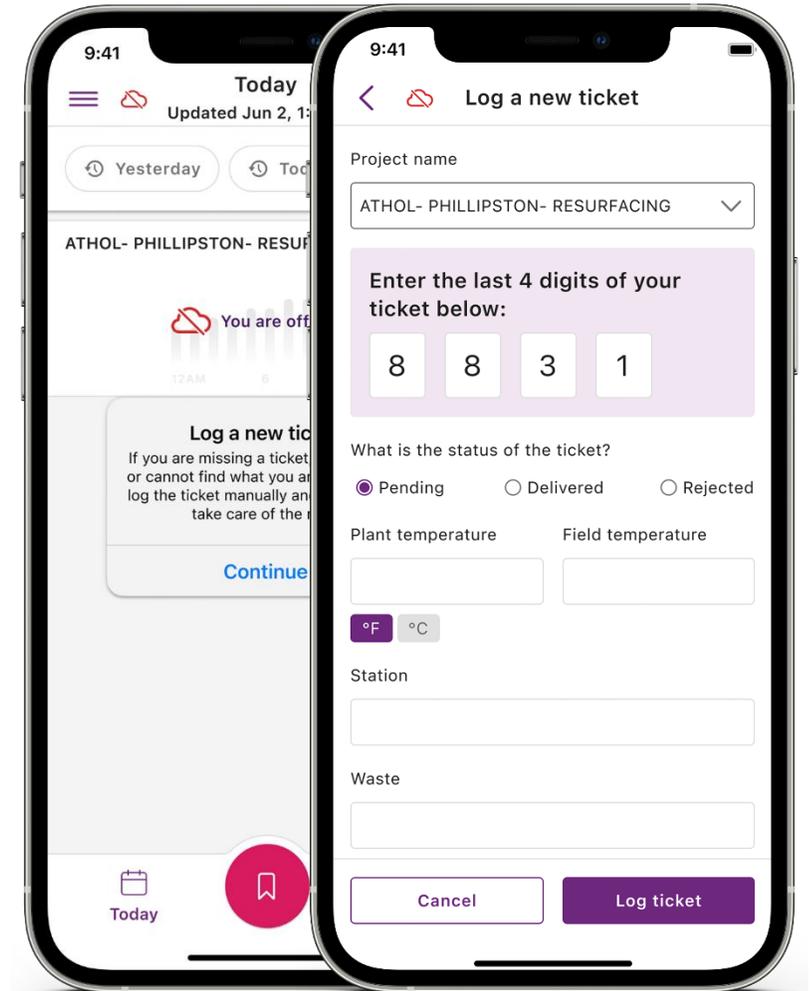

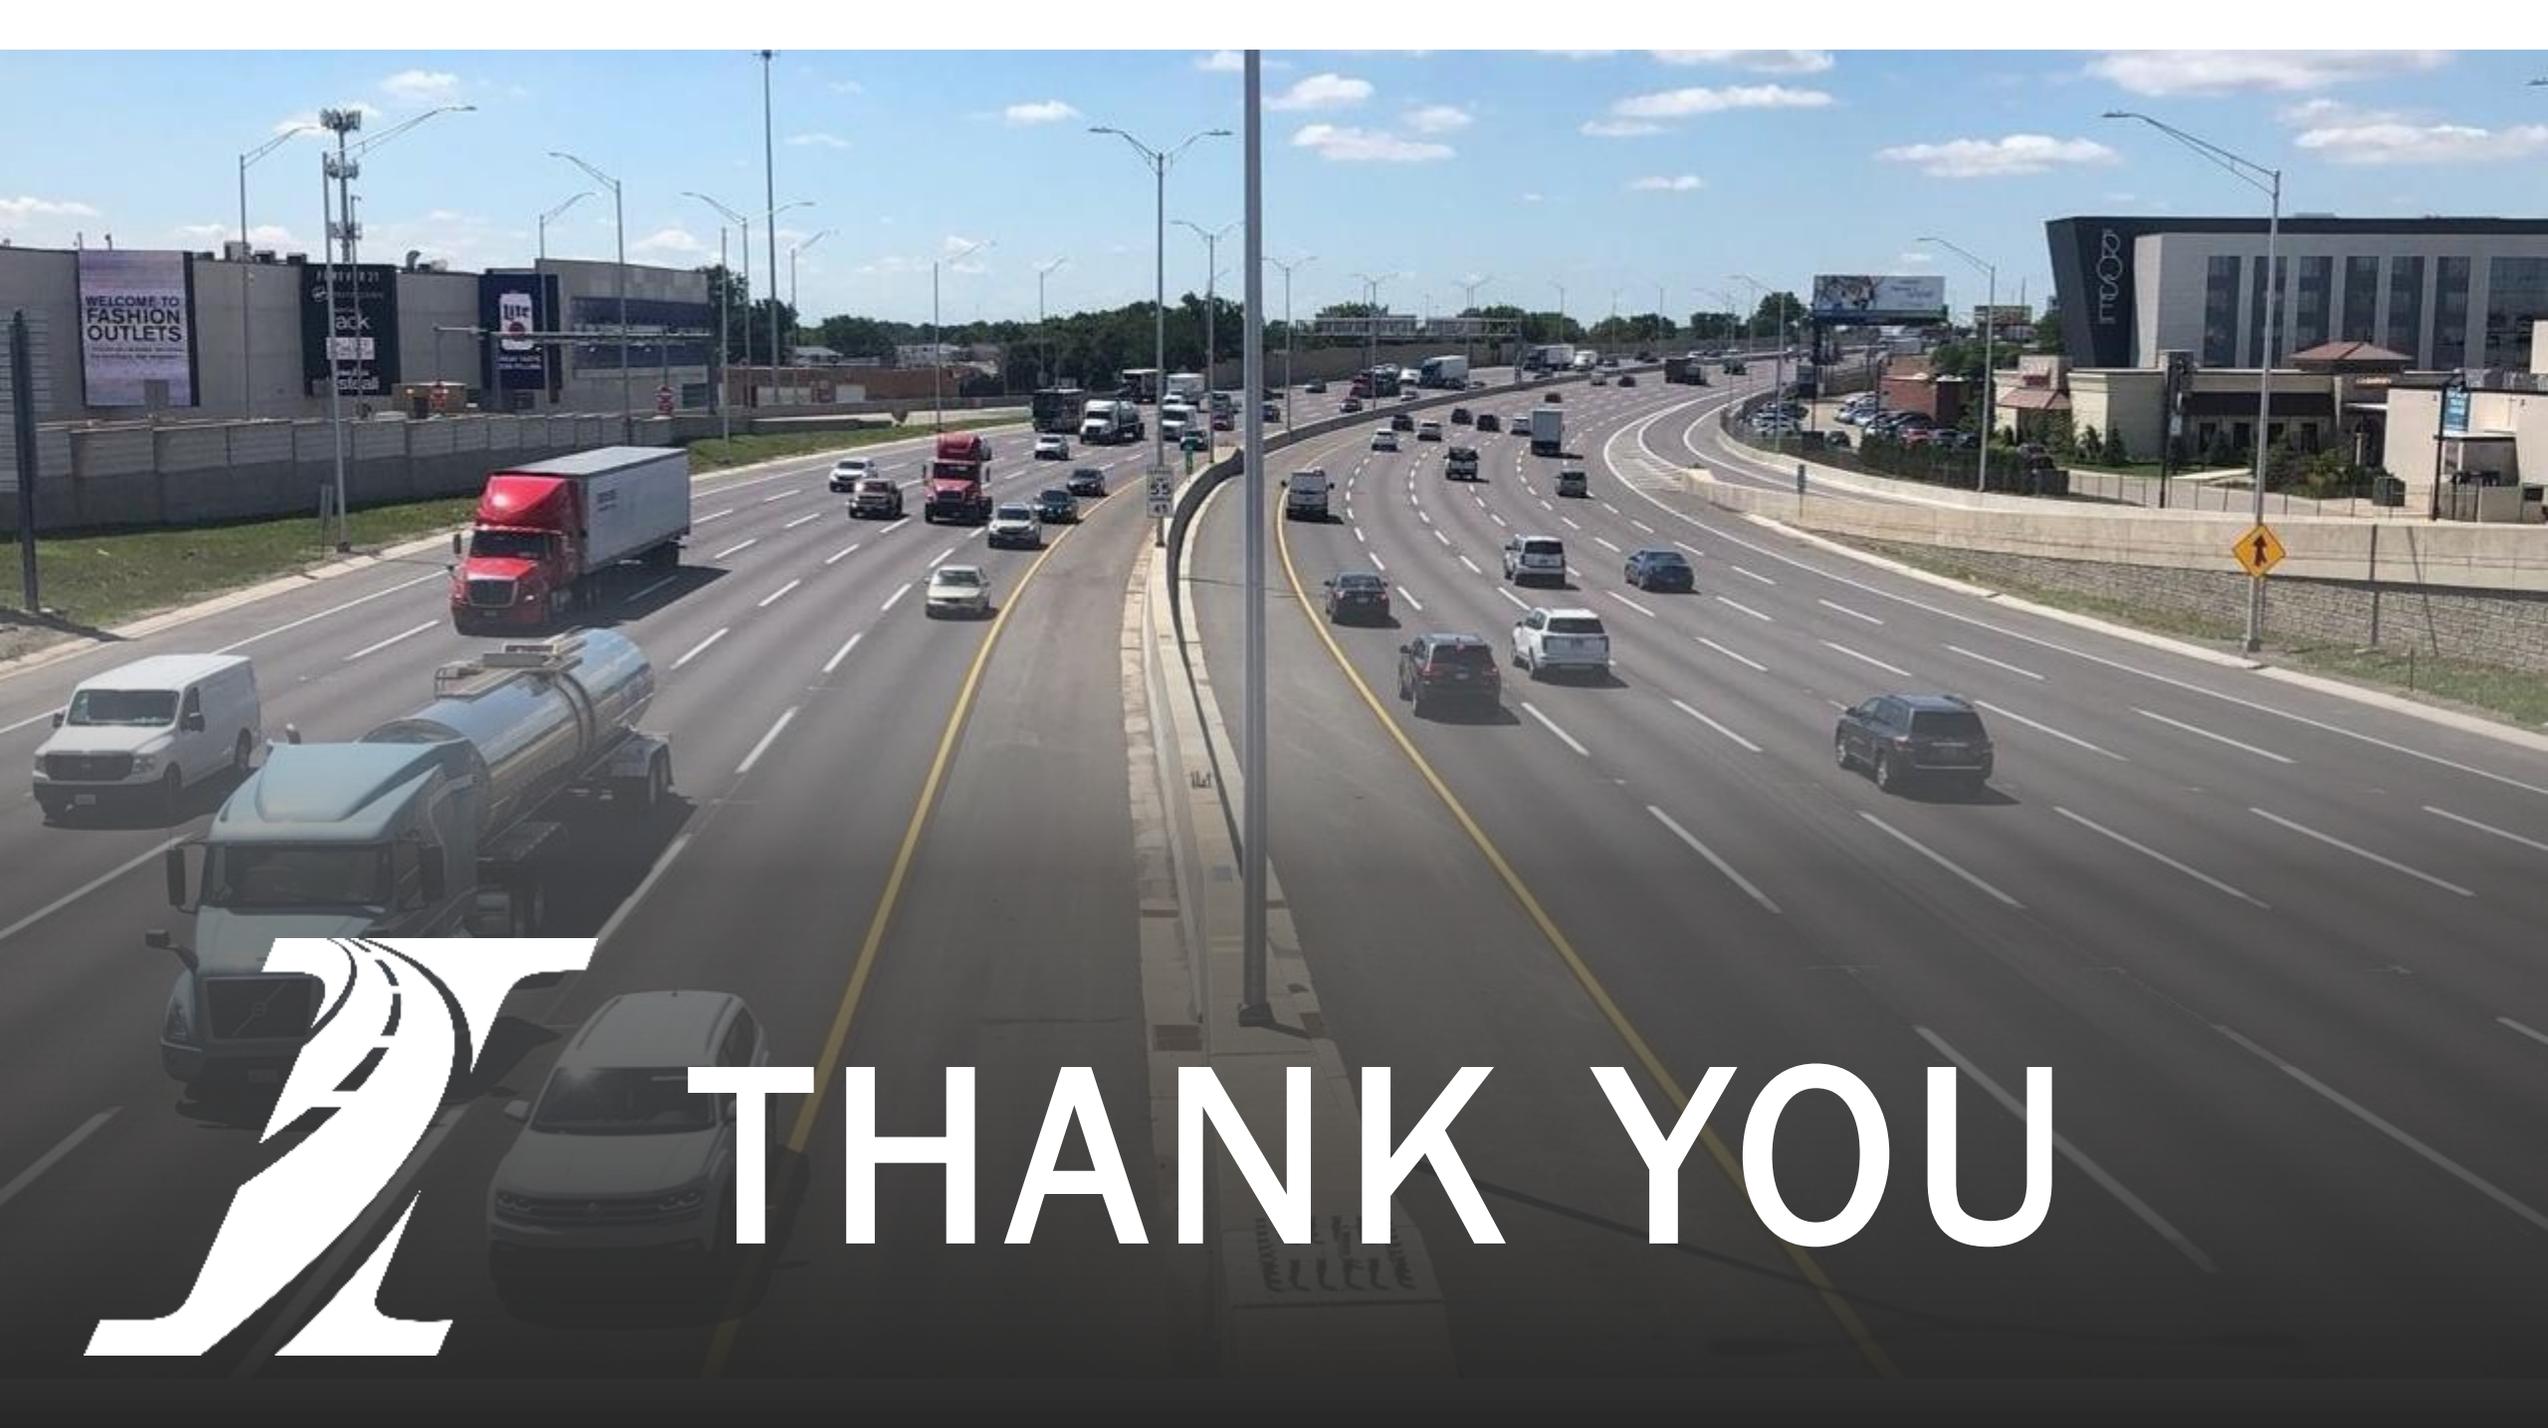

WELCOME TO
FASHION
OUTLETS

ack

Lite

Billboard

OUTLET



THANK YOU
